



26 March 2026

H.E. Im Sethyra

Delegate of the Royal Government in charge as
Director General
General Department of Resettlement
Ministry of Economy and Finance
Royal Government of Cambodia

Your Excellency:

**Loan 4143-CAM: Livable Cities Investment Project
— No Objection to the Social Safeguards Monitoring Report on Land Acquisition and
Involuntary Resettlement (January to September 2025)**

We refer to your Excellency's letter dated 27 October 2025, along with the latest subsequent clarifications received by email on 24 February 2026, requesting our no objection to the social safeguards monitoring report on land acquisition and involuntary resettlement (SMR-LAR) for implementation of the detailed resettlement plan for Bavet Wastewater Treatment Plan and Conveyance Network and Solid Waste Management System subprojects, covering the period from January to September 2025.

The report provides detailed and sufficient information on the implementation of the detailed resettlement plan. We therefore have no objection to your report. The SMR-LAR has already been disclosed on the Asian Development Bank's website and can be accessed at <https://www.adb.org/projects/documents/cam-53199-001-smr-4>.

Mr. Ratha Sann can be contacted at rsann@adb.org, should additional information be required.

Please accept, Your Excellency, the assurances of my highest consideration.

Yours sincerely,

A handwritten signature in black ink, appearing to be 'Siti Hasanah', is located below the text 'Yours sincerely,'.

Siti Hasanah
Unit Head, Project Administration
Water and Urban Development Sector Office
Sectors Department 2

ASIAN DEVELOPMENT BANK

6 ADB Avenue, Mandaluyong City
1550 Metro Manila, Philippines
Tel +63 2 8632 4444
Fax +63 2 8636 2444
www.adb.org

cc: H.E. Ros Seilava, Secretary of State, MEF
H.E. Pen Thirong, Secretary of State, MEF
H.E. Koy Sodany, Permanent Secretary of State, MPWT
H.E. Chhuon Samrith, Under Secretary of State, MEF
H.E. Vong Pisith, Under Secretary of State/ Project Director, MPWT
H.E. Houll Bonnaroth, Director General, GDICDM, MEF
Mr. Meas Sam An, Deputy Director General, GDICDM, MEF
Mr. Chann Thorn, Deputy Director General, GDR, MEF
Mr. Pou Manith, Project Manager, PMU, MPWT
Mr. Kim Sothearith, Director, DMC, GDICDM, MEF
Mr. Non Wattanak, Director, DPPM, GDICDM, MEF
Mr. Kim Chanvibol, Director, RD3, GDR, MEF
Mr. Kong Ratha, Director, DIMDM, GDR, MEF
Mr. Chum Kiry, Deputy Director, DIMDM, GDR, MEF
Mrs. Veng Youim, Deputy Director, DMC, GDICDM, MEF
Mr. Chan Sopanhavorn, Deputy Director, DMC, GDICDM, MEF
Ms. Ieng Sreyleap, Chief, OMC1, DMC, GDICDM, MEF



Ministry of Economy and Finance

General Department of Resettlement

Department of Internal Monitoring and Data Management

Social Safeguards Monitoring Report

Cambodia: Livable Cities Investment Project

**Bavet: Wastewater Treatment Plant and Conveyance
Network and Stormwater Drainage Network and Solid
Waste Management System Subprojects**

Monitoring Period: January 2025 to September 2025

TABLE OF CONTENTS

ABBREVIATIONS.....	3
1. INTRODUCTION.....	4
1.1 BACKGROUND OF THE PROJECT.....	4
1.2 BACKGROUND OF THE SUBPROJECT	4
1.3 PURPOSE OF THE REPORT.....	5
2. INSTITUTIONAL ARRANGEMENT	5
3. SCOPE OF LAND ACQUISITION AND RESETTLEMENT.....	6
4. PROGRESS OF CONTRACT SIGNING AND COMPENSATION PAYMENT.....	7
5. LIVELIHOOD RESTORATION PROGRAM	8
6. DEVELOPMENT OF RESETTLEMENT SITE AND RELOCATION	8
7. IMPLEMENTATION SCHEDULE.....	8
8. GRIEVANCE REDRESS MECHANISM	9
9. PUBLIC CONSULTATION MEETINGS	9
10. CONCLUSION AND RECOMMENDATION	9

List of Table:

Table 1: Summary of the Project and the Subprojects Data and Milestone Dates	5
Table 2: Institutional Roles and Responsibilities of the GDR	6
Table 3: Summary of the IR Impacts of the Subprojects in the DRP	7
Table 4: Summary of Information of Actual Budget Expenditure against the Estimated Budget.....	8
Table 5: Actual and Tentative Implementation Schedule of Resettlement Activities.....	8

List of Figure:

Figure 1: Location of the Target Areas under the Project.....	4
---	---

List of Annexes:

Annex A: Contract Signing Stage	10
Annex B: Compensation Stage.....	16

ABBREVIATIONS


ADB	-	Asian Development Bank
AHs/APs	-	Affected Households/Persons
DIMDM	-	Department of Internal Monitoring and Data Management
DRP	-	Detailed Resettlement Plan
EA	-	Executing Agency
GDR	-	General Department of Resettlement
GRM	-	Grievance Redress Mechanism
IRC	-	Inter-Ministerial Resettlement Committee
IRC-WG	-	Inter-Ministerial Resettlement Committee Working Group
IRP	-	Income Restoration Program
LAR	-	Land Acquisition and Involuntary Resettlement
MEF	-	Ministry of Economy and Finance
MPWT	-	Ministry of Public Works and Transport
PMU	-	Project Management Unit
PGRC	-	Provincial Grievance Redress Committee
RGC	-	Royal Government of Cambodia
SMR	-	Social Safeguards Monitoring Report
SOP	-	Standard Operating Procedures for Externally Financed Projects in Cambodia
USD	-	United States Dollar

1. INTRODUCTION

1.1 BACKGROUND OF THE PROJECT

1. The Livable Cities Investment Project, hereafter referred to as the Project, is financed by the Asian Development Bank (ADB), aiming to support the Royal Government of Cambodia (RGC) in promoting long-term sustainable growth and enhancing urban livability in secondary cities in Cambodia. The Project will address key environmental and infrastructure challenges, thereby facilitating both economic development and improved living conditions for residents. Outputs include: (i) Output 1: policy and regulatory environment improved; (ii) Output 2: urban infrastructure improved; and (iii) Output 3: institutional effectiveness, and governance improved. It shall be noted that only activities under Output 2 will result in the Land Acquisition and Involuntary Resettlement (LAR).
2. The Project will improve access to urban infrastructure through (i) construction of a wastewater treatment plant and sewerage network in Bavet and Poipet, and the expansion of the sewerage network in Kampot; (ii) rehabilitation of existing canals and construction of new stormwater drains in Bavet and Poipet; and (iii) construction of landfills, including sorting of solid waste and composting plants, in Bavet and Poipet.
3. The Project is classified as Category “B” for Involuntary Resettlement (IR) impacts. The loan and grants were approved in December 2021 and became effective in March 2022. The loan and grants will be closed on 31 May 2028. A map showing the target locations/areas under the Project is in Figure 1.

Figure 1: Location of the Target Areas under the Project

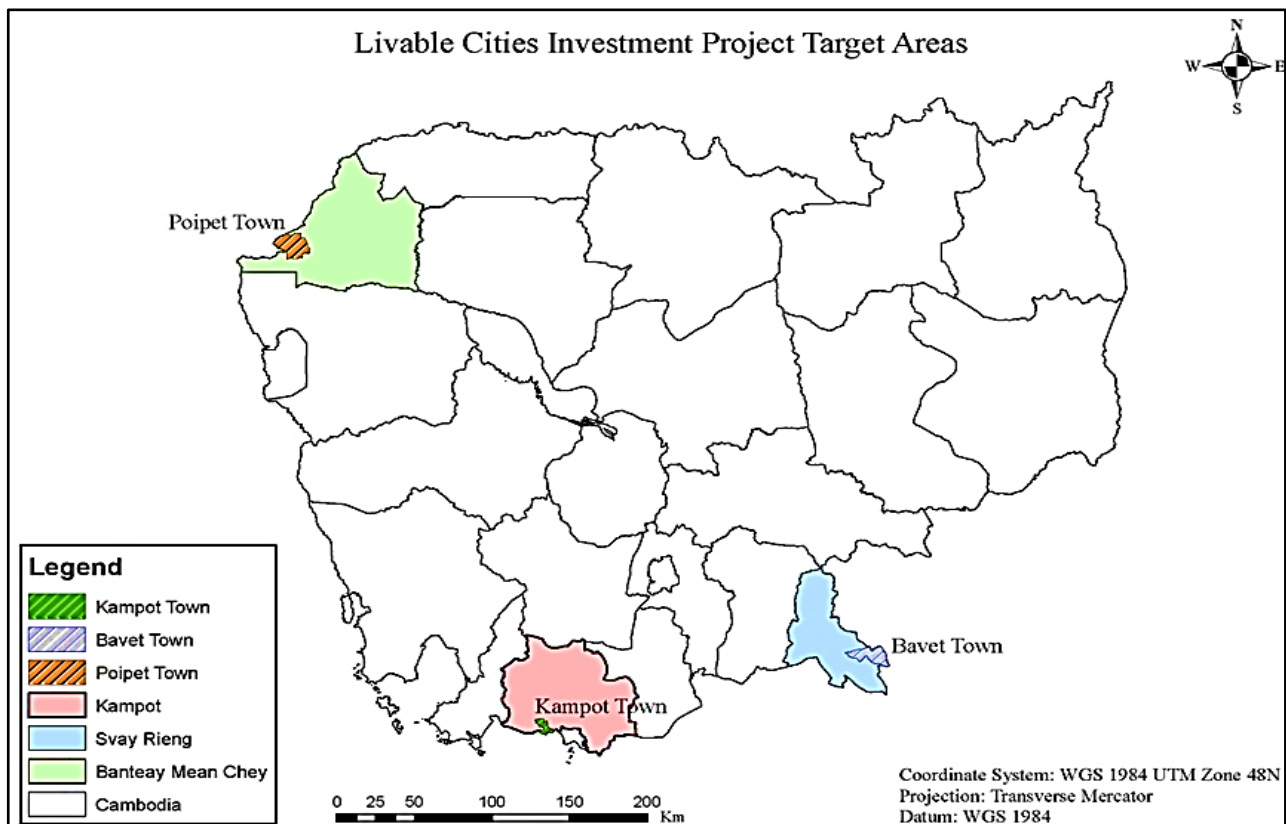

1.2 BACKGROUND OF THE SUBPROJECT

4. This monitoring report covers two subprojects namely: (i) CW-BAV-01: Wastewater Treatment Plant (WWTP) and Conveyance Network and Stormwater Drainage Network and (ii) CW-BAV-02: Solid Waste Management (SWM) System, hereafter referred to as the Subprojects.

5. The outputs for CW-BAV-01 Subproject include (i) construction of a sewerage network comprising a WWTP with a capacity of 3,930 m³/day, and 1,522 household connections; (ii) 9.6 km of new or rehabilitated drainage network, and (iii) sorting and composting plant with a controlled landfill of 516,305 m³ capacity with waste collection vehicles. The outputs of CW-BAV-02 Subproject include (i) construction and operation of a SWM landfill, land gas collection and flaring, leachate collection, transfer and storage, construction of support facilities (office, security guard house, weighbridge, parking lots, fencing, administrative and service buildings, a materials recovery facility (MRF), compost bay, wash bay), internal access road network, sewerage and storm water systems. It also includes the rehabilitation of an access road of 4,816 m from the Junction of National Road 1 to Chark Mtes Village.
6. The DRP for the two subprojects was approved by the Inter-Ministerial Resettlement Committee (IRC) on 31 October 2024 and subsequently endorsed by the ADB on 20 November 2024. The cut-off date for eligibility was established on 12 September 2020. Table 1 summarizes the Project and the Subprojects Data and Milestone Dates.

Table 1: Summary of the Project and the Subprojects Data and Milestone Dates

Project Name	Cambodia: Livable Cities Investment Project
Loan/Grant/Credit Number	4143-CAM(COL)
Date of Approval of Loan and Grant	December 2021
Name of Subprojects	CW-BAV-01: Wastewater Treatment Plant and Conveyance Network and Stormwater Drainage Network Subproject CW-BAV-02: Solid Waste Management System Subproject
Name of Province	Bavet City, Svay Rieng Province
Detailed Design and Demarcation of Land Completed	May 2024
Cut Off Date for Eligibility	12 September 2020
DRP Approved by IRC	31 October 2024
DRP Endorsed by ADB	20 November 2024

1.3 PURPOSE OF THE REPORT

7. The purpose of this Social Safeguards Monitoring Report on Land Acquisition and Involuntary Resettlement (LAR-SMR) is to measure and report on the progress in the implementation of the DRP, identify problems and risks, if any, and measures to mitigate them as well as assess if the compensation and rehabilitation assistance are in accordance with the provisions under the DRP. The Report covers the monitoring period from January 2025 to September 2025.

2. INSTITUTIONAL ARRANGEMENT

8. There have been no changes or deviations in the institutional arrangements set up for the Project and remain the same as specified in the DRP. The Project is implemented by the Ministry of Public Works and Transport (MPWT) as the Executing Agency (EA) through the Project Management Unit (PMU). It is supported by Design and Construction Supervision Consultants (DCSC) to assist the MPWT in the management and implementation of the Project. However, the responsibility for the preparation of the DRP, its implementation and monitoring are undertaken by the GDR in accordance with its mandate.
9. The GDR, as the permanent secretariat of the IRC, is the lead agency directly responsible for the preparation, implementation, monitoring and reporting of the LAR activities under the DRP. The Resettlement Department 3 (RD3) of the GDR has been assigned with undertaking the LAR activities under the Project.

10. The Department of Internal Monitoring and Data Management (DIMDM) of the GDR is responsible for carrying out the internal monitoring and reporting of the implementation of the DRP. Table 2 illustrates the institutional roles and responsibilities of the GDR for undertaking Involuntary Resettlement Safeguards.

Table 2: Institutional Roles and Responsibilities of the GDR

Activities	Responsible Agencies
Finalization of sites/alignments/land boundaries for subproject	EA/PMU, PIU, DCSC
Consultation with communities and APs during project preparation	PMU/ADB/Project Preparation Consultants/ Provincial PIU/GDR
Conducting Census of all APs	GDR, PMU and EA
Conducting DMS	GDR/PRSC-WG
Preparation of draft DRP	GDR/RD3
Preparation of RCS and calculation of replacement cost units	RCS Consultant recruited by GDR
Consultation meetings with all APs and other stakeholders	GDR, IRC-WG and PRSC-WG and local authorities
Endorsement and approval of the DRP	IRC and ADB
Approval of budget for DRP implementation	RGC/MEF
Preparation of Compensation Packages and Contracts	GDR/RD3/DIMDM
Payment of Compensation	GDR, IRC/WG and PRSC/PRSC-WG
Grievance Redress	Local District Administration /GDR/PGRC
Internal Monitoring and Reporting on Implementation of DRP	DIMDM/GDR
Semi-annual Social Safeguards Monitoring Report on the Implementation of the DRP (to ADB)	DIMDM/GDR

3. SCOPE OF LAND ACQUISITION AND RESETTLEMENT

11. There has been no change in the scope or alignment of the civil works for the Subprojects under the Project and hence no update or supplementary DRP was necessary. The implementation of the DRP for the Project is 100% completed and hence, this Report is the final SMR for the Subprojects. The summary of the details on the LAR impacts by category is provided below:

3.1. Impact on AHs

12. In total, 74 AHs/ 286 APs were affected by the Subprojects. None of the AHs had to relocate from their homes. All of them experienced economic impacts only.

3.2. Impact on Land Type

13. The Subprojects affected unused private agricultural land, private residential lands, and some public land. About 4,569.68 m² of private agricultural land owned by 7 AHs and 528.80 m² of residential land of 3 households were impacted. The remaining land of these AHs remained usable. Public land within the ROW was also affected due to widening the access road to the landfill site. None of the land acquired was rented, leased, or uses by indigenous customary land.

3.3. Impact on Structures

14. A total of 41.08 m² of primary structures of 4 AHs/APs was partially affected. No homes of AHs were physically displaced to a new location and all the AHs/APs still had sufficient living space as well as sufficient land without any need for homes, shops (fixed stalls) to be relocated to a new site. The AHs/APs moved back from the construction area to their own land at the same location.

The Subprojects caused partial impacts on secondary structures. Under the solid waste management (SWM) subproject, this included fences of different types (about 410.60m in total,

belong to 16AHs), extended roofs, brick walls, retaining walls (in total of 220.86 m², belong to 16AHs), and 9 spiritual houses, belong to 9AHs. Under the wastewater treatment plant (WWTP) subproject, impacts included 241m of barbed wire fences with wooden posts of 6 AHs, 483.15 m² of storage shelter, kitchen, etc. and one water tank. The pumping station of the wastewater impacted on 60.50m of fence and concrete posts with mesh wire, 18m² of shelter, and one water well. The AHs were able to rebuild these structures on their own land adjacent to the ROW.

3.4. Impact on Crops and Trees

15. No crops were affected. However, 216 trees belonging to 45 AHs were affected. These included 48 fruit trees of 37 AHs and 168 non-fruit trees of 44 AHs.

3.5. Impact on Community and Public Assets

16. No community or public assets were affected.

3.6. Impact on Business and Income

17. The Subprojects partially affected one shop of one AH and two fixed stalls of two AHs. These businesses were moved back out of the ROW to the AHs own land. The affected businesses experience temporary loss of income during the transition period a were compensated for business loss as per the EM.
18. The IR impacts based on category under the Subprojects are summarized in table 3.

Table 3: Summary of the IR Impacts of the Subprojects in the DRP

No.	Impact Type	Quantity (measurement units)
1	Affected Households/Affected Persons	74 AHs/286 APs
2	State-owned Land	Nil
3	Private Agricultural Land (unused)	4,569.68m ² (7 AHs)
4	Residential Land (Partial)	528.80m ² (3 AHs)
5	Main Structures (house, shops and stalls)	41.08m ² (4AHs)
6	Secondary Structures	712.10m (23 AHs) 722.01m ² (29 AHs) and 11 Nos. (11 AHs)
7	Crops	None
8	Trees	216 of 45 AHs
9	Public Facilities	None
10	Loss of Business Income	1 shop and 2 fixed stalls of 3 AHs/13 APs (in total)
11	Income Restoration Program	Nil
12	Relocation (New Site)	Nil

Source: DRP for the Subprojects

4. PROGRESS OF CONTRACT SIGNING AND COMPENSATION PAYMENT

19. The signing of the contracts for the compensation packages was conducted on 24 November 2024. By the end of the reporting period, the contracts for the compensation packages have been signed by all 74 AHs, achieving a completion rate of 100%.
20. Following this, compensation payments to all 74 AHs/286 APs were disbursed on 25 January 2025. The compensation payments totaled 216,010.98 USD compared to the budget of 214,822.48 USD specified in the DRP. The variance of 1,188.50 USD was insignificant. This should be noted that the variance happened due to the slight changes in the re-classification of the land types for one

AH, discovered during the contract signing verification process. However, all non-land assets, including other structures, trees and non-fruit trees, and allowances showed no deviations. There are payments pending. Table 4 shows the details of actual expenditures against the estimated budgets specified in the DRP.

Table 4: Summary of Information of Actual Budget Expenditure against the Estimated Budget

Entitlement Category	Estimated Budget in DRP (\$)	Variance (\$)	Actual Expenditure (\$)	Percentage Disbursed (%)
Unused Private Agricultural Land	86,110.69	1,188.50	87,299.19	101.38%
Residential Land	80,738.00	-	80,738.00	100.00%
Fruit Trees	2,319.75	-	2,319.75	100.00%
Non-fruit Trees	1,635.00	-	1,635.00	100.00%
Shops & Stalls	902.11	-	902.11	100.00%
Primary Structures	440.00	-	440.00	100.00%
Secondary Structures	39,300.83	-	39,300.83	100.00%
Income loss during transition period	2,752.62	-	2,752.62	100.00%
Primary Structure	50.00	-	50.00	100.00%
Shops	50.00	-	50.00	100.00%
Fixed Stalls	100.00	-	100.00	100.00%
Special Allowance for Vulnerable AHs	423.48	-	423.48	100.00%
Total	214,822.48	1,188.50	216,010.98	100.55%

5. LIVELIHOOD RESTORATION PROGRAM

21. There were no AHs who lost any source of their livelihoods permanently under the Subprojects and hence, there was no need for the implementation of the Income Restoration Program (IRP).

6. DEVELOPMENT OF RESETTLEMENT SITE AND RELOCATION

22. There was no physical relocation required and hence there was no need for the development of any resettlement site under the subprojects.

7. IMPLEMENTATION SCHEDULE

23. All compensation payments were completed in January 2025. The acquired land was subsequently handed over to the MPWT on 4 February 2025. All key activities were achieved ahead of the implementation schedule specified in the DRP. Table 5 provides a comparative overview of the actual progress against the tentative implementation schedule in the DRP.

Table 5: Actual and Tentative Implementation Schedule of Resettlement Activities

Activities	Tentative Schedule	Actual Implementation	Remarks
Budget Approval	December 2024	December 2024	
Public Consultation Meetings	January 2025	November 2024 and January 2025	

Contract Signings	January 2025	November 2024	
Compensation Payments	Jan-Feb 2025	January 2025	
Land Handover Letter	March 2025	4 February 2025	

8. GRIEVANCE REDRESS MECHANISM

24. The Grievance Redress Mechanism (GRM) follows the three-step process as described in the DRP for the Project. Aggrieved AHs/APs can lodge complaints at the district, the GDR, and the Provincial levels to seek timely resolution. The authority is vested with the PGRC to make the final administrative decision if any AH/AP is not satisfied with the resolution at the District or the GDR level. If the aggrieved AH/AP is not satisfied with the decision of the District, GDR and PGRC, s/he is free to file a lawsuit at any stage in the competent court (Municipal or Provincial court, as applicable). This GRM process remains the same as provisioned in the DRP.
25. The PGRC was established on 03 June 2024 and is fully functional and operational. As of the end of the monitoring period, there have been no changes in the members of the PRGC.
26. In addition, there have been no formal written complaints lodged by any AHs under the GRM.

9. PUBLIC CONSULTATION MEETINGS

27. During the implementation of the DRP, the public consultation for pre-signing contract was held on 29 and 30 November 2024 at the Bati commune and followed by AH-to-AH level consultations. The consultation prior to the provision of compensation payments, on the other hand, was held on 25 January 2025. The minutes of both meetings in Khmer and in English, attendance lists and pictures of activities are all attached accordingly in Annexes (for the purpose of confidentiality, the names of the AHs/APs should not be disclosed by the ADB)

10. CONCLUSION AND RECOMMENDATION

28. With the handover of the acquired land to MPWT on 4 February and no pending grievances, the implementation of the DRP for the two subprojects is 100% completed. All the key activities were completed ahead of schedule, and no delays were experienced on account of any bottlenecks in the implementation of the DRP. There was no instance of any non-compliance with the provisions in the DRP and hence, no requirement for any corrective action plan during the period of the implementation of the DRP.
29. Therefore, it is concluded that the DRP of the Project has been fully and successfully completed, and this monitoring report marks the final report on the implementation of the DRP.



Annexes

Annex A: Contract Signing Stage

A. Minutes of Meeting (Khmer Version-1st Consultation)

ព្រះរាជាណាចក្រកម្ពុជា ជាតិ សាសនា ព្រះមហាក្សត្រ

គណៈកម្មការអន្តរក្រសួង
ដោះស្រាយវេជ្ជប័ណ្ណ

កំណត់ហេតុប្រជុំ

ប្រជុំពិគ្រោះយោបល់ជាសាធារណៈ ជាមួយប្រជាពលរដ្ឋដែលទទួលបានវេជ្ជប័ណ្ណដោយសារ
គម្រោងអភិវឌ្ឍន៍ទីក្រុងក្នុងតំបន់ស្រះស្រព ភូមិក្រុងស្រះស្រពខេត្តស្វាយរៀង(មុនពេលចុះកិច្ចសន្យាផ្តល់ប្រាក់សំណង)
ឆ្នាំពីរពាន់ម្ភៃបួន ខែវិច្ឆិកា ថ្ងៃទីម្ភៃប្រាំបួន វេលាម៉ោង ៨និង៣០នាទីព្រឹកនៅទីតាំងផ្ទះប្រជាពលរដ្ឋ ក្នុង
ភូមិព្រៃទប់សង្កាត់ច្រកម្តេសក្រុងបាវិតខេត្តស្វាយរៀងមានបើកកិច្ចប្រជុំផ្សព្វផ្សាយជាសាធារណៈមុនពេលចុះកិច្ចសន្យា
ផ្តល់ប្រាក់សំណងជូនប្រជាពលរដ្ឋដែលទទួលបានវេជ្ជប័ណ្ណដោយសារគម្រោងមុនដំណើរការអនុវត្តការងារចុះកិច្ចសន្យា
ក្រោមការដឹកនាំដោយ **លោក យ៉ក់ ប៊ុនហេង** អនុប្រធានក្រុមការងារគណៈកម្មការអន្តរក្រសួងដោះស្រាយវេជ្ជប័ណ្ណ
ប៉ះពាល់សមាសភាពចូលរួមមានក្រុមការងារគណៈកម្មការអន្តរក្រសួងដោះស្រាយវេជ្ជប័ណ្ណប៉ះពាល់ក្រុមការងារអនុគណៈ
កម្មការខេត្ត

ព្រមទាំងព្រមទាំងអាជ្ញាធរមូលដ្ឋានដែលពាក់ព័ន្ធគម្រោងនិងប្រជាពលរដ្ឋដែលរងផលប៉ះពាល់ដោយសារគម្រោង
(ដូចមានជូនភ្ជាប់នូវបញ្ជីមានភ្ជាប់មកជាមួយស្រាប់)

ជាកិច្ចចាប់ផ្តើមលោក ខាំ វិទ្យា នាយករដ្ឋបាលសាលាក្រុងបាវិត
បានមានមតិស្វាគមន៍ជាមួយប្រជាពលរដ្ឋដែលមានវត្តមានក្នុងកិច្ចប្រជុំដោយបានជម្រាបជូនប្រជាពលរដ្ឋដែលរងផលប៉ះពាល់
ទាំងអស់ថាថ្ងៃនេះយើងជួបជុំគ្នាដើម្បីផ្សព្វផ្សាយពីចុះកិច្ចសន្យាផ្តល់ប្រាក់សំណងជូនបងប្អូនដែលរងផលប៉ះពាល់ដោយសារគម្រោង
ដូច្នេះសូមចូលរួមទាំងអស់គ្នាដើម្បីឱ្យគម្រោងដំណើរការបានល្អ។ ជាកិច្ចបន្តលោក
យ៉ក់ ប៊ុនហេង បានលើកឡើងបញ្ជាក់ពីការចុះកិច្ចសន្យាផ្តល់ប្រាក់សំណងជូនបងប្អូនទាំងអស់ដែលបានចូលរួមប្រជុំ
ព្រឹកនេះ ហើយក្រោយពីបញ្ចប់កិច្ចប្រជុំត្រូវបន្តធ្វើកិច្ចសន្យាផ្តល់ប្រាក់សំណងជូនបងប្អូនទៀតដូច្នេះក្នុងពេលចុះសន្យានឹងបានដឹង
ពីសំណងដែលត្រូវទទួលបានគ្រប់គ្នា ក្រោយពីបញ្ចប់កិច្ចហើយក្រុមការងារ និងរៀបចំឯកសារបញ្ជូនទៅថ្នាក់ដឹកនាំ
ដើម្បីដកប្រាក់បើកជូនបងប្អូន ។

ជាកិច្ចបន្ត ខ្ញុំសូមទុកពេលផ្តល់លទ្ធភាពជូនប្រជាពលរដ្ឋលើកជាសំណួរ ៖

- សំណួរប្រជាពលរដ្ឋ

១- លោកស្រី តៅ ស៊ុកក្រ រស់នៅភូមិច្រកម្តេស សង្កាត់ច្រកម្តេស ក្រុងបាវិត

- បានសួរថា តើសំណងប៉ះពាល់របស់គាត់សងនៅពេលណា? សំណួរពេលផ្តល់សំណងបានឆាប់

លោក យ៉ក់ ប៊ុនហេងបានជម្រាបទៅគាត់ថាសំណងបានឆាប់លុះត្រាតែបងប្អូនចូលរួមសហការជាមួយក្រុមការងារបាន
ល្អ នោះសំណងនឹងបានឆាប់។

២- លោក ប៉ុល សំអាត ភូមិច្រកម្តេសសង្កាត់ច្រកម្តេសបានសួរថាក្រោយចុះកិច្ចសន្យាផ្តល់ប្រាក់សំណងហើយតើគាត់
ពេលដែលក្រុមការងារចុះធ្វើកិច្ចសន្យាផ្តល់ប្រាក់សំណងបានល្អ និងបន្តដំណើរការនៅក្រោយពេលបញ្ចប់កិច្ចប្រជុំ
នេះ។

កិច្ចប្រជុំបានបញ្ចប់នៅវេលាម៉ោង ១០ ព្រឹកនាថ្ងៃខែឆ្នាំដែលប្រកបដោយភាពសប្បាយរីករាយនិងស្មារតីទទួល
ខុសត្រូវ។

បានឃើញ និងឯកភាព

ប្រធានអង្គប្រជុំ



យ៉ក់ ប៊ុនហេង

អ្នកធ្វើកំណត់ហេតុ



អេង វិទ្យា

ព្រះរាជាណាចក្រកម្ពុជា
ជាតិ សាសនា ព្រះមហាក្សត្រ

គណៈកម្មការអន្តរក្រសួង
ដោះស្រាយផលប៉ះពាល់

កំណត់ហេតុប្រជុំ

ប្រជុំពិគ្រោះយោបល់ជាសាធារណៈ ជាមួយប្រជាពលរដ្ឋដែលទទួលបានផលប៉ះពាល់ដោយសារ
គម្រោងអភិវឌ្ឍន៍វិស័យកសិកម្មឱ្យបានរស់នៅ ស្ថិតក្នុងភូមិសាស្ត្រខេត្តស្វាយរៀង(មូលដ្ឋានចុះកិច្ចសន្យាផ្តល់ប្រាក់សំណង)

ឆ្នាំពីរពាន់ម្ភៃបួន ខែវិច្ឆិកា ថ្ងៃទីសាមសិប វេលាម៉ោង ៩ ព្រឹក នៅទីតាំង សាលាសង្កាត់បាទី ក្រុងបាទី ខេត្តស្វាយរៀងមានបើកកិច្ចប្រជុំផ្សព្វផ្សាយជាសាធារណៈមុនពេលចុះកិច្ចសន្យាផ្តល់ប្រាក់សំណងជូនប្រជាពលរដ្ឋដែលទទួលបានផលប៉ះពាល់ដោយសារគម្រោងមុនដំណើរការអនុវត្តការងារចុះកិច្ចសន្យាក្រោមការដឹកនាំដោយ **លោក យក់ ប៊ុនហេង អនុប្រធានក្រុមការងារគណៈកម្មការអន្តរក្រសួងដោះស្រាយផលប៉ះពាល់សហគមន៍** ក្រុមការងារគណៈកម្មការអន្តរក្រសួងដោះស្រាយផលប៉ះពាល់ក្រុមការងារអនុគណៈកម្មការខេត្ត ព្រមទាំងព្រមទាំងអាជ្ញាធរមូលដ្ឋានដែលពាក់ព័ន្ធគម្រោង និងប្រជាពលរដ្ឋដែលបានផលប៉ះពាល់ដោយសារគម្រោង(ដូចមានជូនភ្ជាប់នូវបញ្ជីវត្តមានភ្ជាប់មកជាមួយស្រាប់)។

ជាកិច្ចចាប់ផ្តើមលោក ខាំ វិទ្យុ នាយករដ្ឋបាលសាលាក្រុងបាទីបានមានមតិស្វាគមន៍ជាមួយប្រជាពលរដ្ឋដែលមានវត្តមានក្នុងកិច្ចប្រជុំដោយបានជម្រាបជូនប្រជាពលរដ្ឋដែលបានផលប៉ះពាល់ទាំងអស់ថាថ្ងៃនេះយើងជួបជុំគ្នាដើម្បីផ្សព្វផ្សាយពីចុះកិច្ចសន្យាផ្តល់ប្រាក់សំណងជូនបងប្អូនដែលបានផលប៉ះពាល់ដោយសារគម្រោង ដូច្នេះសូមចូលរួមទាំងអស់គ្នាដើម្បីឱ្យគម្រោងដំណើរការបានល្អ។ ជាកិច្ចបន្ទាប់លោក យក់ ប៊ុនហេង បានលើកឡើងបញ្ហាពីការចុះកិច្ចសន្យាផ្តល់ប្រាក់សំណងជូនបងប្អូនទាំងអស់ដែលបានចូលរួមប្រជុំព្រឹកនេះ ហើយក្រោយពីបញ្ចប់កិច្ចប្រជុំត្រូវបន្តធ្វើកិច្ចសន្យាជូនបងប្អូនបន្តទៀតដូច្នេះក្នុងពេលចុះសន្យានឹងបានដឹងពីសំណងដែលត្រូវទទួលបានគ្រប់គ្នាក្រោយពីបញ្ចប់កិច្ចហើយក្រុមការងារ និងរៀបចំឯកសារបញ្ជូនទៅថ្នាក់ដឹកនាំដើម្បីជកប្រាក់បើកជូនបងប្អូន ។

ជាកិច្ចបន្ត ខ្ញុំសូមទុកពេលផ្តល់លទ្ធភាពជូនប្រជាពលរដ្ឋលើកជាសំណួរ ៖

- សំណួរប្រជាពលរដ្ឋ

១- លោក ខុន យាន រស់នៅភូមិថ្មាញ សង្កាត់បាទី ក្រុងបាទី

-បានសួរថា តើក្រោយពីចុះកិច្ចសន្យាហើយ បើកប្រាក់នៅពេលណា?

លោក យក់ ប៊ុនហេងបានជម្រាបថាក្រោយពីចុះកិច្ចសន្យាហើយ ក្រុមការងារបន្តរៀបចំឯកសារជូនថ្នាក់ដឹកនាំសុំជកប្រាក់បើកជូនតែម្តង។

២- លោក ចាន់ សារ៉ាន ភូមិថ្មាញ សង្កាត់បាទី បានសួរថាក្រោយពីបើកប្រាក់រួចតើទុករយៈពេលប៉ុន្មានថ្ងៃសម្រាប់ការរុះរើលុះ លោក យក់ ប៊ុនហេងបានជម្រាបគាត់ថាក្រោយពីទទួលប្រាក់ហើយ ទុករយៈពេល១ខែសម្រាប់ការរុះរើលុះ

ទីបញ្ចប់លោកខាំ វិទ្យុបានសំណូមពរដល់បងប្អូនប្រជាពលរដ្ឋទាំងអស់មេត្តាជួយសហការជាមួយក្រុមការងារនៅពេលដែលក្រុមការងារចុះធ្វើកិច្ចសន្យាផ្តល់ប្រាក់សំណងឱ្យបានល្អ និងបន្តដំណើរការនៅក្រោយពេលបញ្ចប់កិច្ចប្រជុំនេះ។

កិច្ចប្រជុំបានបញ្ចប់នៅវេលាម៉ោង ១និង៣០នាទីព្រឹកនាថ្ងៃ ខែ ឆ្នាំដែលប្រកបដោយភាពសប្បាយរីករាយនិងស្មារតីទទួលខុសត្រូវ។

បានឃើញ និងឯកភាព

ប្រធានអង្គប្រជុំ



យក់ ប៊ុនហេង

អ្នកធ្វើកំណត់ហេតុ



នេ វិថា

Kingdom of Cambodia

Nation Religion King



Inter-Ministerial of
Resettlement Committee

Minutes of Meeting

**Public Consultation Meeting with Affected Households under the Livable City Development
Project in Svay Rieng Province (Before Signing the Compensation Contract)**

(1) Two Thousand Twenty Four November, Twenty Nine 8:30am at the residence of the affected household in Phum Prey torb, Sangkat Chrok Mtes, Bavet, Svay Rieng Province and (2) Two Thousand Twenty Four November, Thirty 9am at Sangkat Bati Administration Office, Bavet, Svay Rieng Province, a public meeting was held to inform households about the compensation contract prior to its signing and contract implementation process, under the leadership of Mr. Youk Bunheng, Deputy Chairman of the Inter-Ministerial Resettlement Committee(IRC). The participants included the members of the Inter-Ministerial Resettlement Committee, the Provincial Sub-Committee, as well as relevant local authorities and AHs by the project (as attached in the attendance list).

First of all, Mr. Kham Rithy, Director of Bavet Branch Administration, welcomed the whole meeting. He informed AHs that the purpose of the meeting was to publicly announce the upcoming signing of compensation contracts and invited all AHs to cooperate and make the project run smoothly. Next, Mr. Yuk Bunheng mentioned the process for signing of compensation contract to the attended households and preparations would continue after the meeting. Each AHs would be informed of the compensation amount they are entitled to. The working group will be preparing documents to the relevant authorities to request the release of compensation for AHs.

Next, we left the opportunity to AHs to raise questions:

Question& Answer (29, November 2024)

1. Mrs. Tao Sopheak resided in Phum Chrok Mtes, Sangkat Chrok Mtes, Bavet.
 - Asked: When will the compensation be paid? She requested that the payment be made as soon as possible.Mr. Yuk Bunheng answered that the compensation would be paid promptly, provided that households cooperate with the working group.

2. Mr. Bol Somart resided in Phum Chrok Mtes, Sangkat Chrok Mtes, Bavet.
 - Asked: After signing the contract, can they cut down their trees?Mr. Yuk Bunheng answered to wait until receiving the compensation before cutting it down

Question & Answer (30, November, 2024)

1. Mr. Khun Yean resided in Phum Thnanh, Sangkat Bati, Bavet.
 - Asked: After signing the contract, when will the compensation be paid?Mr. Youk Bunheng answered that after the contract are signed, the working group will prepare the documents to the relevant authorities to request the release of compensation.
2. Mr. Chan Saren resided in Phum Thnanh, Sangkat Bati, Bavet.
 - Asked: After receiving compensation, how many days will we have to pack and move?Mr. Youk Bunheng answered that affected households will have one month from the date of receiving compensation to pack and relocate.

Last, Mr. Kham Rithy urged all affected households to cooperate with the working group responsible for signing the compensation contracts to ensure the project proceeds smoothly. The meeting ended on the same day in a friendly and responsible atmosphere.

Seen and Endorsed By

Chairman of the Meeting

Minute Meeting Taker

Mr. Youk Bunheng

Chai Vila

D. Attendant List and Photos During Public Consultation:

ပြည်ထောင်စုကြီး
တစ် နယ်စပ် ပြည်ထောင်စု

အထောက်အကူပြုသူ
အထောက်အကူပြုသူအားလုံး၏

ပဏ္ဍိတအဖွဲ့အစည်းအဖွဲ့ဝင်များ (၆/၁၁/၂၀၂၄)
၆/၁၁/၂၀၂၄

စာ.နံ	အမည်	အသက်	အလုပ်	ရက်စွဲ	ရက်စွဲ
၁			၆၈	၆/၁၁/၂၀၂၄	
၂			၆၈	၆/၁၁/၂၀၂၄	
၃			၆၈	၆/၁၁/၂၀၂၄	
၄			၆၈	၆/၁၁/၂၀၂၄	
၅			၆၈	၆/၁၁/၂၀၂၄	
၆			၆၈	၆/၁၁/၂၀၂၄	
၇			၆၈	၆/၁၁/၂၀၂၄	
၈			၆၈	၆/၁၁/၂၀၂၄	
၉			၆၈	၆/၁၁/၂၀၂၄	

၁၀					
၁၁					
၁၂					
၁၃					
၁၄					
၁၅					
၁၆					
၁၇					
၁၈					
၁၉					
၂၀					
၂၁					
၂၂					
၂၃					

ပြည်ထောင်စုကြီး
တစ် နယ်စပ် ပြည်ထောင်စု

အထောက်အကူပြုသူ
အထောက်အကူပြုသူအားလုံး၏

ပဏ္ဍိတအဖွဲ့အစည်းအဖွဲ့ဝင်များ (၆/၁၁/၂၀၂၄)
၆/၁၁/၂၀၂၄

စာ.နံ	အမည်	အသက်	အလုပ်	ရက်စွဲ	ရက်စွဲ
၁			၆၈	၆/၁၁/၂၀၂၄	
၂			၆၈	၆/၁၁/၂၀၂၄	
၃			၆၈	၆/၁၁/၂၀၂၄	
၄			၆၈	၆/၁၁/၂၀၂၄	
၅			၆၈	၆/၁၁/၂၀၂၄	
၆			၆၈	၆/၁၁/၂၀၂၄	
၇			၆၈	၆/၁၁/၂၀၂၄	
၈			၆၈	၆/၁၁/၂၀၂၄	
၉			၆၈	၆/၁၁/၂၀၂၄	

၁၀					
၁၁					
၁၂					
၁၃					
၁၄					
၁၅					
၁၆					
၁၇					
၁၈					
၁၉					
၂၀					
၂၁					
၂၂					
၂၃					

၂၄					
၂၅					
၂၆					
၂၇					
၂၈					
၂၉					
၃၀					
၃၁					

E. Photos of Activities



Annex B: Compensation Stage

A. Minutes of Meeting (Khmer Version)



**ព្រះរាជាណាចក្រកម្ពុជា
ជាតិ សាសនា ព្រះមហាក្សត្រ**

**គណៈកម្មការអន្តរក្រសួងជាតិស្រាវជ្រាវ
ផលប៉ះពាល់ដោយសារការប្រែប្រួលអាកាសធាតុ**

កំណត់ហេតុ

**ស្តីពីកិច្ចពិគ្រោះយោបល់ជាសាធារណៈជាមួយប្រជាពលរដ្ឋផលប៉ះពាល់ដោយសារការប្រែប្រួលអាកាសធាតុ
ក្នុងគម្រោងអោយចង់រស់នៅ
ស្ថិតក្នុងភូមិសាស្ត្រខេត្តស្វាយរៀង(ដំណាក់កាលមុនបើកប្រាក់ឧបត្ថម្ភគោលនយោបាយ)**

ឆ្នាំពីរពាន់ម្ភៃប្រាំ ខែមករាថ្ងៃទីបី វេលាម៉ោងប្រាំបី ព្រឹកនៅស្នាក់ការកណ្តាលនៃក្រុមប្រឹក្សាភិបាល ក្រុងបាវិត
ខេត្តស្វាយរៀង។

មានកិច្ចប្រជុំស្តីពីកិច្ចពិគ្រោះយោបល់ជាសាធារណៈជាមួយប្រជាពលរដ្ឋផលប៉ះពាល់ដោយសារការប្រែប្រួល
អាកាសធាតុក្នុងគម្រោងអោយចង់រស់នៅ ស្ថិតក្នុងភូមិសាស្ត្រខេត្តស្វាយរៀង ដំណាក់កាលមុនបើកប្រាក់ឧបត្ថម្ភគោល
នយោបាយដែលដឹកនាំដោយលោក ហ៊ឺវ បញ្ញាសិទ្ធិ ប្រធានក្រុមការងារគណៈកម្មការអន្តរក្រសួង
ព្រមទាំងមាន

ការចូលរួមពីក្រុមការងារអនុគណៈកម្មការដោះស្រាយផលប៉ះពាល់ខេត្ត លោកតំណាងនាយកដ្ឋានត្រួតពិនិត្យផ្ទៃ
ក្នុង អាជ្ញាធរមូលដ្ឋានដែលពាក់ព័ន្ធ និងតំណាងប្រជាពលរដ្ឋផលប៉ះពាល់(ដូចមានភ្ជាប់ជាមួយបញ្ជីវត្តមាន
ស្រាប់)។ ជាកិច្ចចាប់ផ្តើមលោក ហ៊ឺវ បញ្ញាសិទ្ធិបានមានមតិស្វាគមន៍ចំពោះអង្គប្រជុំទាំងមូល និងបានលើកឡើង
នីតិវិធីនៃការដោះស្រាយផលប៉ះពាល់ដោយសារការប្រែប្រួលអាកាសធាតុក្នុងគម្រោងអោយចង់រស់នៅ ដែលចាប់ផ្តើមពីការ
ងារអង្កេតវាស់វែងលម្អិតការចុះកិច្ចសន្យា និងការបើកប្រាក់ឧបត្ថម្ភគោលនយោបាយ ជាពិសេសលោកបានលើ
កឡើងពីការសិក្សាអត្រាតម្លៃដីក្នុងស្រុកដែលជាមូលដ្ឋាននៃការគណនាសំណងជូនគ្រួសាររងផលប៉ះពាល់ដោយសារ
ការប្រែប្រួលអាកាសធាតុ។ ជាកិច្ចបន្ត

លោក វ៉ា វិទ្យា នាយករដ្ឋបាលសាលាក្រុងបាវិត បានសំដែងនូវអំណរសាទរចំពោះគម្រោងនេះ ដែលជាការរួម
ចំណែកយ៉ាងធំធេងចំពោះការអភិវឌ្ឍន៍ហេដ្ឋារចនាសម្ព័ន្ធរូបវិទ្យា ក៏ដូចជាអនាម័យ និងបរិស្ថានរបស់ខេត្តតាំងមូ
លហើយលោកបានបញ្ជាក់ទៅប្រជាពលរដ្ឋដែលរងផលប៉ះពាល់ដែលត្រូវបើកប្រាក់ថ្លៃនេះថា នៅពេលទទួល
យកប្រាក់ត្រូវពិនិត្យអោយបានច្បាស់លាស់ រាប់អោយគ្រប់ចំនួនមុននឹងចាកចេញ ។ ជាទីបញ្ចប់លោក ហ៊ឺវ
បញ្ញាសិទ្ធិ ក៏បានលើកឡើងពីកាតព្វកិច្ចរបស់គ្រួសាររងផលប៉ះពាល់ ពេលតម្រូវឱ្យពួកគាត់ធ្វើការរុះរើសំណង់
ដែលរងផលប៉ះពាល់ដោយខ្លួនឯង ក្នុងរយៈពេល ៣០ថ្ងៃបន្ទាប់ពីទទួលបានប្រាក់ឧត្តម្ភោសនយោបាយរួច។

កិច្ចប្រជុំពិគ្រោះយោបល់នេះ បានបញ្ចប់ នៅវេលាប្រាំបួនព្រឹកនៅថ្ងៃខែឆ្នាំដែលក្រោមបរិយាកាសរីករាយ
ស្និទ្ធស្នាលនិងទទួលខុសត្រូវខ្ពស់។

បានឃើញ ឯកភាព

ប្រធានអង្គប្រជុំ



ហ៊ឺវ បញ្ញាសិទ្ធិ

អ្នកធ្វើកំណត់ហេតុ



យ៉ក់ ប៊ុនហេង

B. Minutes of Meeting (English Version)

Kingdom of Cambodia

Nation Religion King



Inter-Ministerial of
Resettlement Committee

Minutes of Meeting

**Public Consultation Meeting with the Affected Households under the Livable City Development
Project in Svay Rieng Province (Pre-Policy Subsidy Phase)**

- (1) Two Thousand Twenty Five January, Third, 8am at the Phum Prey Tub Administration Office, Sangkat Chhak Mtes, Bavet, Svay Rieng Province, and (2) 2pm at Sangkat Bati Administration Office, Bavet, Svay Rieng Province. A public meeting was held with the affected households, presided over by Mr. Hav Panhaseth, Chairman of the Inter-Ministerial Committee. The participants included the Provincial Resettlement Sub-Committee, the General Inspectorate Department, as well as relevant local authorities and AHs (as attached in the attendance list).

First of all, Mr. Hav Panhaseth welcomed the whole meeting. He explained the process and procedure of the land acquisition and resettlement affected by the livable city development project, starting from the detailed measurement survey, signing of the compensation contract, and policy subsidy. He emphasized that compensation calculations are based on the replacement cost study(RCS). Next, Mr. Kham Rithy, Director of Bavet Branch Administration, expressed his gratitude toward the project, which is a major contribution to the development of infrastructure, as well as the sanitation and environment of the entire province. He advised the affected households who would receive the payment on the same day to carefully verify and count the amount before leaving.

Last, Mr. Hav Panhaseth mentioned the obligations of affected households, requiring them to dismantle the affected structures themselves within 30 days of receiving the policy subsidy.

The meeting ended on the same day in a friendly and responsible atmosphere.

Seen and Endorsed By

Chairman of the Meeting

Minute Meeting Taker

Mr. Heav Panha Seth

Chai Vila

C. Attendant list:

ព្រះរាជាណាចក្រកម្ពុជា
ជាតិ សាសនា ព្រះមហាក្សត្រ

គណៈកម្មាធិការអន្តរក្រសួង
អគ្គនាយកដ្ឋានការងារសង្គម

03/01/2025

បញ្ជីអ្នកបម្រើការងារសង្គមសម្រាប់ថ្ងៃទី ០៣ ខែ មករា ឆ្នាំ ២០២៥

ល.រ	ឈ្មោះ	ភេទ	អង្គភាព	តួនាទី	ស្នាមមេដៃ
1					
2					
3					
4					
5					
6					
7					
8					
9					

10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				

ព្រះរាជាណាចក្រកម្ពុជា
ជាតិ សាសនា ព្រះមហាក្សត្រ

គណៈកម្មាធិការអន្តរក្រសួង
អគ្គនាយកដ្ឋានការងារសង្គម

ថ្ងៃទី ០៣ ខែ ០១ ឆ្នាំ ២០២៥

បញ្ជីអ្នកបម្រើការងារសង្គមសម្រាប់ថ្ងៃទី ០៣ ខែ មករា ឆ្នាំ ២០២៥

ល.រ	ឈ្មោះ	ភេទ	អង្គភាព	តួនាទី	លេខទូរស័ព្ទ	ស្នាមមេដៃ
1						
2						
3						
4						
5						
6						
7						
8						
9						
10						
11						
12						
13						
14						
15						
16						
17						
18						
19						
20						
21						
22						
23						

24				
25				
26				
27				
28				
29				
30				
31				

D. Photos of Activities:

